


SRDP SCHEDULE

June 27, 2018



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	Resource Names	Document Number
0		530 SRDP Schedule	1224 days?	Wed 1/25/17	Mon 10/4/21		26%		
1		External Milestones	767 days	Thu 6/1/17	Sun 5/10/20		0%		
2		ALMA	259 days	Fri 9/29/17	Fri 9/28/18		0%		
11		VLA	624 days	Wed 9/13/17	Mon 2/3/20		0%		
22		VLAAS	690 days	Mon 9/18/17	Sun 5/10/20		0%		
31		DMS	260 days	Mon 10/2/17	Fri 9/28/18		0%		
38		NRAO Management	136 days	Thu 6/1/17	Thu 12/7/17		100%		
44		POP	172 days	Thu 2/1/18	Fri 9/28/18		0%		
45		5.6.15 Proj. Sci. Appointed	0 days	Wed 4/25/18	Wed 4/25/18	65	100%		
46		5.6.18 Scope/LD/OpsCon	75 days	Thu 2/1/18	Wed 5/16/18	93	0%		
47		7.5.20 PM/SE Docs	0 days	Mon 2/19/18	Mon 2/19/18	73,83	100%		
48		7.5.21 CoDR Doc set	0 days	Thu 4/19/18	Thu 4/19/18	116	100%		
49		5.6.16 Initiation Closes / CoDR	0 days	Mon 5/28/18	Mon 5/28/18	108	0%		
50		5.6.19 Cycle 1 defined / L1 Req.	37 days	Thu 5/10/18	Fri 6/29/18	131	0%		
51		5.6.17 Ops Mgr. Appointed	68 days	Wed 6/27/18	Fri 9/28/18	66	0%		
52		Project Initiation	410 days?	Wed 1/25/17	Tue 8/21/18		93%		
121		Wave 1	31.65 mons	Thu 5/31/18	Mon 11/2/20	52	0%		
122		Operations Plan Development	60 days	Wed 8/1/18	Tue 10/23/18	70	0%		
127		Wave 1: New Mexico DA Recruitment	1 day?	Fri 3/15/19	Fri 3/15/19		0%		
128		Wave 1: Heuristics Research Topics	1 day	Thu 5/31/18	Thu 5/31/18		0%		
131		Wave 1: L1 Def	26 days	Fri 5/25/18	Fri 6/29/18		0%		
132		Wave 1: L2 Definition and Design Phase	71 days	Fri 5/25/18	Fri 8/31/18	131	0%		
146		Wave 1: Implementation/verif	7.55 mons	Mon 9/3/18	Mon 4/1/19	132	0%		
147		Wave 1: Validation	6 mons	Mon 9/3/18	Fri 2/15/19	132	0%		
148		Pilot Operations Readiness Review	1 day	Wed 5/15/19	Wed 5/15/19		0%		
149		Pilot Operations	66 days	Mon 6/3/19	Mon 9/2/19		0%		
150		Operations Readiness Review	1 day?	Tue 10/1/19	Tue 10/1/19	149F5+4 wks	0%		
151		Wave 1: Operations Deployment	1 wk	Fri 10/25/19	Thu 10/31/19	150,152SS-1 wk	0%		
152		Wave 1: Operations	13.1 mons	Fri 11/1/19	Mon 11/2/20		0%		
153		Wave 1: Deployment Review (lessons learned)	1 day?	Fri 1/24/20	Fri 1/24/20	152SS+3 mons	0%		
154		Wave 2	686 days?	Mon 2/18/19	Mon 10/4/21		0%		

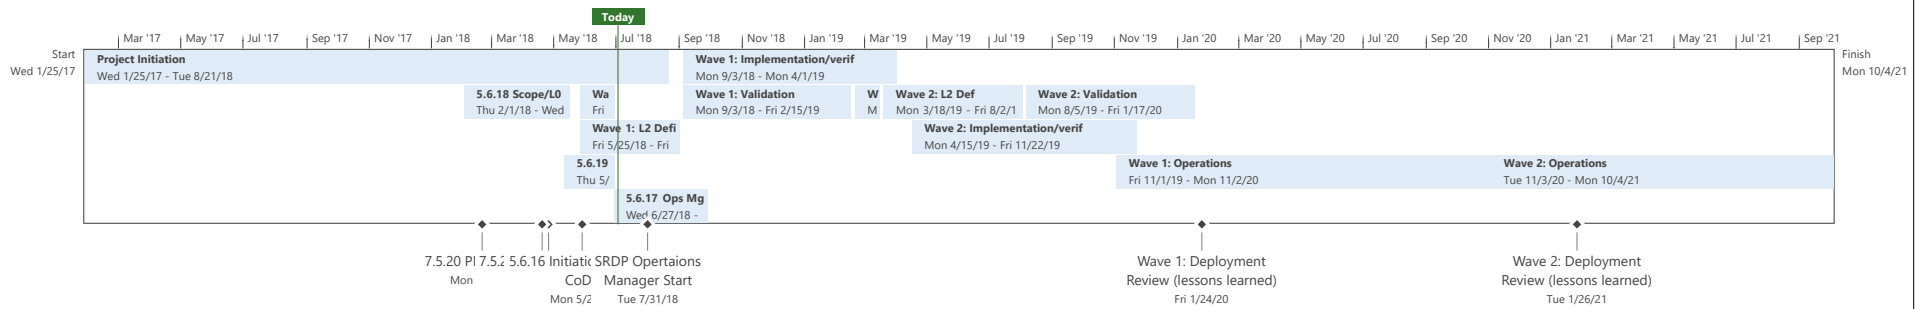
